





ID		Task Mode	Task Name	Duration	Start	Finish	Timeline														
							Sep	Qtr 4, 2025			Qtr 1, 2026			Qtr 2, 2026			Qtr 3, 2026			Qtr 4, 2026	
							Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
38			A/C Thermal Calculation	29 days	Tue 10/21/25	Fri 11/28/25															
39			Stress & flexibility analysis for high pressure pipes	15 days	Tue 12/9/25	Mon 12/29/25															
40			Maintenance Lifting Points Layout and Details	15 days	Tue 12/9/25	Mon 12/29/25															
41			3D MODEL	15 days	Tue 12/9/25	Mon 12/29/25															
42			Drawing	61 days	Tue 10/7/25	Tue 12/30/25															
43			Preparation & Submission	61 days	Tue 10/7/25	Tue 12/30/25															
44			Equipment Layout	44 days	Tue 10/7/25	Fri 12/5/25															
45			Piping Layout	30 days	Wed 11/19/25	Tue 12/30/25															
46			Equipment & Procurement Related	65 days	Tue 10/7/25	Mon 1/5/26															
47			Line List	20 days	Mon 10/20/25	Fri 11/14/25															
48			Preparation & Submission	20 days	Mon 10/20/25	Fri 11/14/25															
49			Line List	20 days	Mon 10/20/25	Fri 11/14/25															
50			Instrument List	40 days	Mon 11/3/25	Fri 12/26/25															
51			Preparation & Submission	40 days	Mon 11/3/25	Fri 12/26/25															
52			Instrument List	10 days	Mon 11/3/25	Fri 11/14/25															
53			Vendor Docs of Instrument	10 days	Mon 12/15/25	Fri 12/26/25															
54			Valve List	40 days	Mon 11/3/25	Fri 12/26/25															
55			Preparation & Submission	40 days	Mon 11/3/25	Fri 12/26/25															
56			Valve List	10 days	Mon 11/3/25	Fri 11/14/25															
57			Vendor Docs of Valve	5 days	Mon 12/22/25	Fri 12/26/25															
58			Container	20 days	Tue 10/7/25	Mon 11/3/25															
59			Preparation & Submission	20 days	Tue 10/7/25	Mon 11/3/25															
60			Datasheet of Container	20 days	Tue 10/7/25	Mon 11/3/25															
61			Electrical Auxiliary Component (Lighting and Power)	26 days	Tue 10/7/25	Tue 11/11/25															
62			Preparation & Submission	26 days	Tue 10/7/25	Tue 11/11/25															
63			Datasheet of Electrical Auxiliary Component (Lighting and Power)	26 days	Tue 10/7/25	Tue 11/11/25															
64			PLC and HMI Panel Component (Major Component)	51 days	Fri 10/17/25	Fri 12/26/25															
65			Preparation & Submission	51 days	Fri 10/17/25	Fri 12/26/25															
66			Datasheet of PLC and HMI Panel Component (Major Component)	20 days	Fri 10/17/25	Thu 11/13/25															
67			PLC Outline Panel Drawing	10 days	Mon 12/15/25	Fri 12/26/25															
68			Motor Control Center (MCC)	50 days	Thu 10/16/25	Wed 12/24/25															
69			Preparation & Submission	50 days	Thu 10/16/25	Wed 12/24/25															
70			Datasheet of Motor Control Center (MCC)	25 days	Thu 10/16/25	Wed 11/19/25															
71			MCC Outline Panel Drawing	12 days	Tue 12/9/25	Wed 12/24/25															
72			SWRO System (Vessel + Membrane)	60 days	Tue 10/14/25	Mon 1/5/26															
73			Preparation & Submission	58 days	Tue 10/14/25	Thu 1/1/26															

Project: 12803_Taltal Water Tre
Date: Fri 10/31/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

Page 2

ID		Task Mode	Task Name	Duration	Start	Finish	Sep	Qtr 4, 2025				Qtr 1, 2026			Qtr 2, 2026			Qtr 3, 2026			Qtr 4, 2026		
								Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	
74			Datasheet SWRO System (Vessel + Membrane)	10 days	Tue 10/14/25	Mon 10/27/25																	
75			GA of SWRO System Skid	5 days	Fri 12/26/25	Thu 1/1/26																	
76			RO High Feed Pump	39 days	Fri 10/17/25	Wed 12/10/25																	
77			Preparation & Submission	39 days	Fri 10/17/25	Wed 12/10/25																	
78			Datasheet of RO High Pressure Pump	20 days	Fri 10/17/25	Thu 11/13/25																	
79			GAD of RO High Pressure Pump	14 days	Fri 11/21/25	Wed 12/10/25																	
80			CIP / Flushing Pump	56 days	Fri 10/17/25	Fri 1/2/26																	
81			Preparation & Submission	56 days	Fri 10/17/25	Fri 1/2/26																	
82			Datasheet of CIP / Flushing Pump	20 days	Fri 10/17/25	Thu 11/13/25																	
83			GA of CIP / Flushing Skid Pump	10 days	Mon 12/22/25	Fri 1/2/26																	
84			Antisclant Dosing Pump	51 days	Fri 10/17/25	Fri 12/26/25																	
85			Preparation & Submission	51 days	Fri 10/17/25	Fri 12/26/25																	
86			Datasheet of Antisclant Dosing Pump	20 days	Fri 10/17/25	Thu 11/13/25																	
87			GA of Antisclant Dosing Skid Pump	5 days	Mon 12/22/25	Fri 12/26/25																	
88			Cartridge Filter	53 days	Thu 10/23/25	Mon 1/5/26																	
89			Preparation & Submission	53 days	Thu 10/23/25	Mon 1/5/26																	
90			Datasheet of Cartridge Filter	25 days	Thu 10/23/25	Wed 11/26/25																	
91			GAD of Cartridge Filter	7 days	Fri 12/26/25	Mon 1/5/26																	
92			CIP Cartridge Filter	53 days	Thu 10/23/25	Mon 1/5/26																	
93			Preparation & Submission	53 days	Thu 10/23/25	Mon 1/5/26																	
94			Datasheet of CIP Cartridge Filter	20 days	Thu 10/23/25	Wed 11/19/25																	
95			GAD CIP Cartridge Filter	7 days	Fri 12/26/25	Mon 1/5/26																	
96			1st Stage Turbo	44 days	Tue 10/28/25	Fri 12/26/25																	
97			Preparation & Submission	44 days	Tue 10/28/25	Fri 12/26/25																	
98			Datasheet of 1st Stage Turbo	20 days	Tue 10/28/25	Mon 11/24/25																	
99			GAD 1st Stage Turbo	10 days	Mon 12/15/25	Fri 12/26/25																	
100			2nd Stage Turbo	44 days	Tue 10/28/25	Fri 12/26/25																	
101			Preparation & Submission	44 days	Tue 10/28/25	Fri 12/26/25																	
102			Datasheet of 2nd Stage Turbo	20 days	Tue 10/28/25	Mon 11/24/25																	
103			GAD 2nd Stage Turbo	10 days	Mon 12/15/25	Fri 12/26/25																	
104			CIP / Flushing Tank	46 days	Fri 10/31/25	Fri 1/2/26																	
105			Preparation & Submission	46 days	Fri 10/31/25	Fri 1/2/26																	
106			Datasheet of CIP / Flushing Tank	20 days	Fri 10/31/25	Thu 11/27/25																	
107			GA of CIP / Flushing Tank	10 days	Mon 12/22/25	Fri 1/2/26																	
108			Antiscalant Dosing Tank	46 days	Fri 10/31/25	Fri 1/2/26																	
109			Preparation & Submission	46 days	Fri 10/31/25	Fri 1/2/26																	
110			Datasheet of Antiscalant Dosing Tank	20 days	Fri 10/31/25	Thu 11/27/25																	
111			GA of Antiscalant Dosing Tank	10 days	Mon 12/22/25	Fri 1/2/26																	

Project: 12803_Taltal Water Tre
Date: Fri 10/31/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone


Deadline

Progress

Manual Progress

Page 3

ID		Task Mode	Task Name	Duration	Start	Finish	Qtr 4, 2025				Qtr 1, 2026			Qtr 2, 2026			Qtr 3, 2026			Qtr 4, 2026		
							Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
112			CIP Tank Heater	42 days	Fri 10/31/25	Mon 12/29/25																
113			Preparation & Submission	42 days	Fri 10/31/25	Mon 12/29/25																
114			Datasheet of CIP Tank Heater	20 days	Fri 10/31/25	Thu 11/27/25																
115			GAD of CIP Tank Heater	11 days	Mon 12/15/25	Mon 12/29/25																
116			Procurement	248 days	Wed 10/15/25	Fri 9/25/26																
252			Inspection & Testing Plan (ITP)	7 days	Tue 12/23/25	Wed 12/31/25																
253			Fabrication	181 days	Fri 1/2/26	Fri 7/31/26																
254			BW Fabrication (Penang)	181 days	Fri 1/2/26	Fri 7/31/26																
255			Antiscalant Dosing Pump Skid	27 days	Thu 5/28/26	Sat 6/27/26																
256			Container	46 days	Sat 1/31/26	Wed 3/25/26																
257			SWRO System Skid	27 days	Fri 1/2/26	Mon 2/2/26																
258			Electrical	14 days	Thu 4/30/26	Fri 5/15/26																
259			Factory Acceptace Test (FAT)	2 days	Thu 7/30/26	Fri 7/31/26																
260			Shipping	0 days	Mon 8/3/26	Mon 8/3/26																
261			Ready to Ship to Project Site (Malaysia)	0 days	Mon 8/3/26	Mon 8/3/26																
262			Installation (by Client)	0 days	Tue 10/7/25	Tue 10/7/25																
263			Site Supervision & Commissioning Supervision	21 days	Sat 9/26/26	Fri 10/16/26																
264			Operator Training	9 days	Sat 10/17/26	Sun 10/25/26																
265			Final Documentation & Close out	30 days	Mon 10/26/26	Tue 11/24/26																

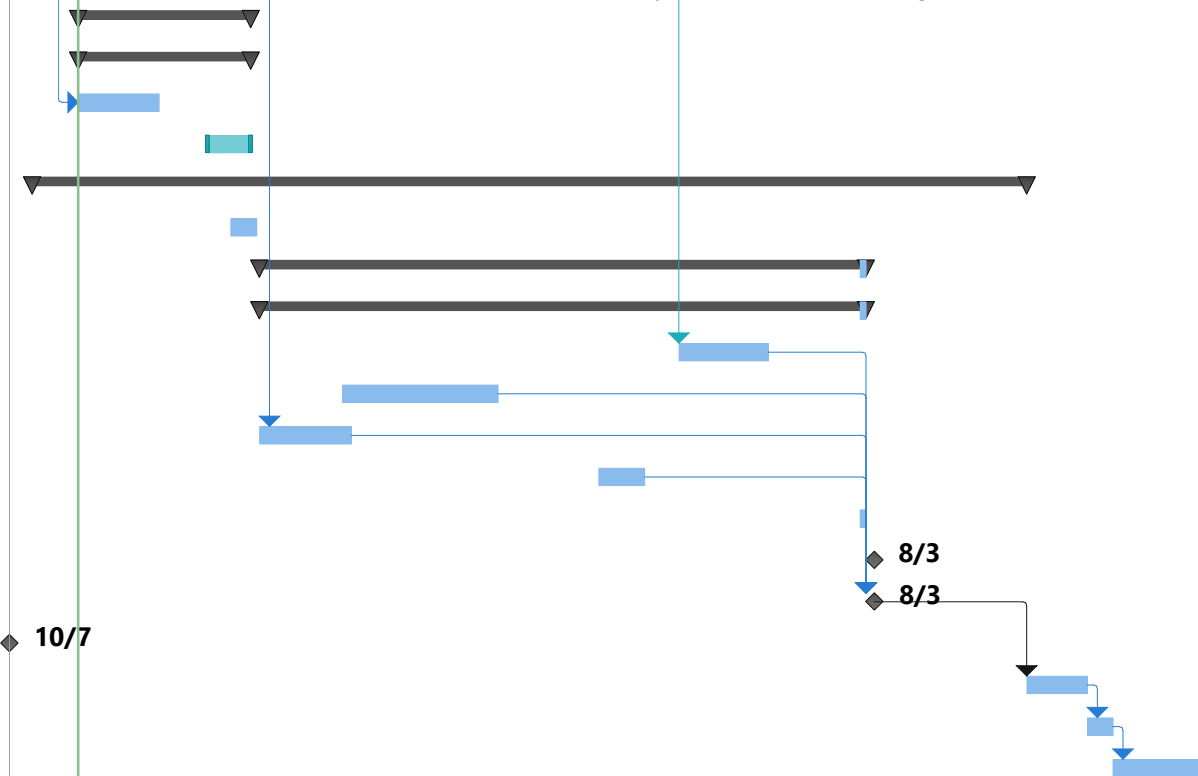

Project: 12803_Taltal Water Tre
Date: Fri 10/31/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Inactive Milestone

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

Page 4
